

The Road Ahead

July 27, 2015 Issue 8

A Newsletter on the River/San Marcos/Heideke Street Project



Staff Contacts

Jose (Joe) R. Ramos
City Engineer
830-401-2337

jramos@seguintexas.gov

Nate Garza
Projects Manager
830-401-2402

ngarza@seguintexas.gov

Pam Herrera
Public Works Assistant
830-401-2776

pherrera@seguintexas.gov


Wade Bolton
Projects Inspector
830-401-2493

wbolton@seguintexas.gov

Previous Project Updates:

[www.seguintexas.gov/
public_works/detail/
capital_projects/](http://www.seguintexas.gov/public_works/detail/capital_projects/)

INCLEMENT WEATHER MAY ALTER SCHEDULE
THANK YOU FOR YOUR CONTINUED PATIENCE

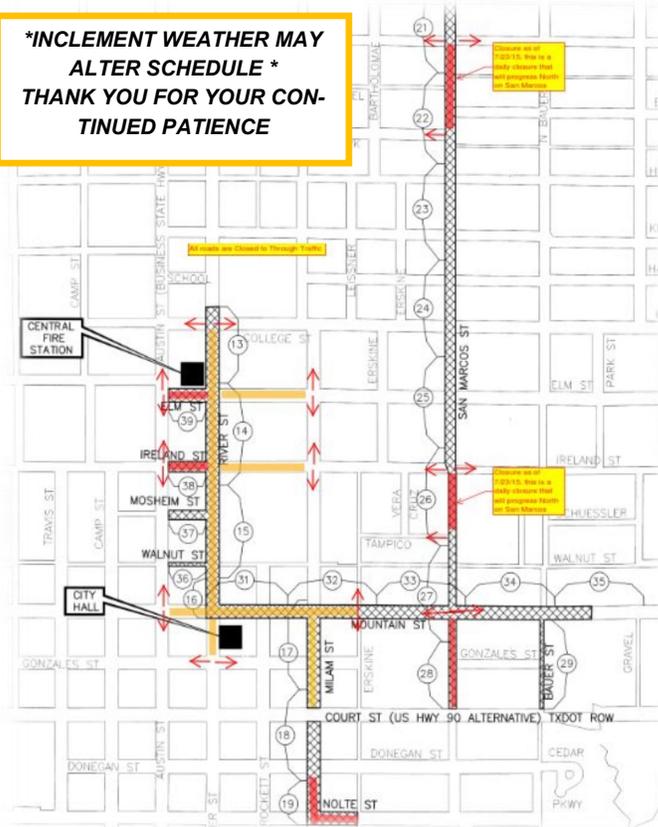

Map Info:

- ⇒ Project area marked with **black 'XXX'**
- ⇒ **Complete Street Closures - "Red"**
- ⇒ **Impacted Streets - "Yellow"**
- ⇒ **NOLTE ST. CLOSED** (Crockett to Erskine)
- ⇒ **MILAM ST. CLOSED** (Donegan to Nolte)
- ⇒ **ELM ST. CLOSED**
- ⇒ **IRELAND ST. CLOSED**

COURT STREET

The installation of the new drainage culvert is almost complete. City officials will meet with TxDOT to finalize how to conduct the street repairs. We anticipate at least 6 weeks of road construction in the area after all of the tests and analysis are considered.

ROAD CONSTRUCTION:

Ongoing excavation and base installation work on Elm, Ireland, Mountain (400-600 blocks), San Marcos (100-200 blocks), and possibly Bauer. Driveways *may not* be usable at these locations during certain times of the day, but ramps will be placed before the end of the day.

CURB CREWS:

Curb work is complete where road base has been installed.

SIDEWALK/DRIVEWAY CREWS:

Flatwork is currently being installed heading east on Mountain St. to Erskine St.

WATER INSTALLATION:

Water utility crews are working on the 700-800 block of N. San Marcos and will continue onto Kingsbury. Residents will be notified by door hanger in advance of water outages.

DRAINAGE INSTALLATION:

Main trunk line is being installed on the 400 block of N. San Marcos, and crews are working their way north. Second crew is following close behind installing curb inlets and laterals.

*****MOTORISTS MAY EXPERIENCE DAILY BLOCK CLOSURES IN THESE AREAS. THE CONTRACTOR MAY REQUEST THAT YOU DO NOT PARK ON AFFECTED STREET(S) WHILE THE WORK IS BEING DONE.*****



www.seguintexas.gov
