


Geronimo Creek Sewer Project - Phase V Oak Village North Subdivision Construction Update



Volume 1, Issue 12 - Week ending November 9, 2012

WHAT'S GOING ON?

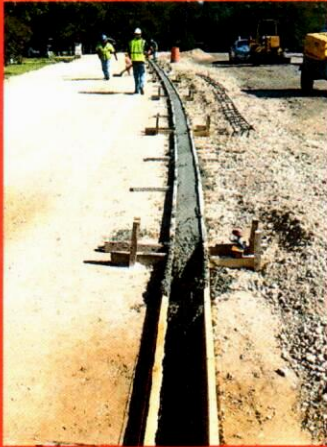

Ribbon Curb Installation ↑

Red Oak: The Curb crew is installing ribbon curb and are preparing to begin restoring driveways approaches. This process may take up to 3 days and you may not be able to park in your driveway. We are hopeful that the this process will

only take 2 days, but please be prepared for 3. If you or anyone you know needs to be able to park in their driveway each night, please let us know and we will try to plan accordingly.

Lone Oak: The Road crew is compacting base material in half road increments. There will always be a passing lane available.

Twin Oak: The Utility crew continues to install the sewer main between Red Oak and White Oak. The Road crew is compacting base material between Red Oak and White Oak. *Please use the detour on Lone Oak.*

White Oak: The Utility crew is installing the water line.

Water line installation →



City of Seguin Holiday Closure

Monday, November 12th -
Veteran's Day

Thursday, November 22nd &
Friday, November 23rd -
Thanksgiving Holiday

*There will not be a newsletter
issued on Friday, November 23rd.*

REMINDERS:

CONTINUE TO PLACE GARBAGE OUT
FOR PICKUP BY 6:00 A.M. ON
TUESDAY MORNINGS.

FOR THE SAFETY OF WORKERS
PLEASE ADHERE TO ALL DETOUR OR
CONSTRUCTION SIGNAGE.

HAVE YOU RETURNED THE "CONSENT
TO INSTALL SEWER TAP" FORM TO THE
CITY? IF YOU NEED ANOTHER FORM,
PLEASE CONTACT US.

IF YOU KNOW A RESIDENT NOT
RECEIVING THESE NEWSLETTERS,
PLEASE REFER THEM TO THE WEBSITE
OR CALL/EMAIL THE CITY TO BE ADDED
TO THE DISTRIBUTION LIST.

DON'T GET CAUGHT UP IN RUMORS ~
FIND OUT THE FACTS! IF YOU HAVE A
QUESTION OR CONCERN ABOUT THE
PROJECT USE STAFF CONTACTS OR VISIT
THE OVN WEBSITE ON THE CITY OF
SEGUIN'S WEB PAGE.
CLICK ON PUBLIC WORKS
CLICK ON CAPITAL PROJECTS

Salinas Technologies, LTD., Utility Crew will be working Saturday, November 10, 2012 on Twin Oak.

Construction and Detours fuel tempers and lead to unfortunate event.....

An unfortunate event occurred this week in which costly equipment owned by Salinas Technologies, Ltd., was damaged as a result of an upset property owner. Construction and detours have led to a great deal of frustration and low tolerance levels by many OVN residents. However, we must continue to work together to see this project to fruition. The City cannot ignore conduct that may jeopardize the safety of the contractor, its equipment, workers or the general public. Therefore, we remind you that your first point of contact should be Nathan or Wade (**STAFF CONTACTS**) to respond and remedy any potential situation that may lead to an unfortunate event and result in law enforcement being summoned. *Thank you for your cooperation!*

You asked...We answered

Q. What are the hours of construction?

A. Typical construction hours are 8:00 a.m. to 5:00 p.m. However, during daylight savings time, the contractor is allowed to work from dawn to dusk, in order to maintain the scheduled deadlines for the project.

SALINAS' HOLIDAY SCHEDULE

November 12th - Construction
November 22nd - No Construction
November 23rd - No Construction

STAFF CONTACTS

NATHAN (NATE) GARZA PROJECTS MANAGER NGARZA@SEGUINTEXAS.GOV	830.401.2402
JOSE (JOE) RAMOS CITY ENGINEER JRAMOS@SEGUINTEXAS.GOV	830.401.2337
WADE BOLTON PROJECTS INSPECTOR WBOLTON@SEGUINTEXAS.GOV	830.401.2493
PAM HERRERA PROJECTS ASSISTANT PHERRERA@SEGUINTEXAS.GOV	830.401.2776

WEB SITE
WWW.SEGUINTEXAS.GOV
